

One governance gap repeating six times, not six expensive contractors.

A ~\$230M contractor programme was billing roughly \$5–6M a year above the assessment benchmark. The cause was not which contractors held the work — it was the absence of rate-book enforcement, which meant replacing them would have reproduced it.

INDUSTRY	ENGAGEMENT CONTEXT	ROLE	DURATION
Energy & utilities — electric distribution	Consulting · large US investor-owned utility	Independent commercial assessment (pre-RFP)	6 weeks

THE SITUATION

- A five-year renewal of the overhead-construction contracts was approaching, against a rate book five years out of date.
- Ambiguous work descriptions and time-based billing made the exposure real but unquantified, with no competitive-tension mechanism in the contract.
- Any diagnosis had to pinpoint where governance failed across 482 rate-book items and six contractors without boiling the ocean.

MY CONTRIBUTION

I led the assessment end to end — designing the three-step commercial-impact method, analysing twelve months of approved spend across roughly 565,000 transactions, quantifying above-market billing, isolating its structural root cause, and converting the diagnosis into a five-pillar contracting framework and a phased roadmap tied to the RFP critical path.

THE JUDGMENT THAT MATTERED

A rate comparison is only useful when the work and its measurement units are genuinely comparable. I weighted each contractor's rates by their own transaction volumes, and held the finding together as one integrated opportunity rather than splitting it into a list of individually deniable line items.

EXHIBIT 1 Spend concentration across the rate book

Pareto of the ~\$230M portfolio · directional


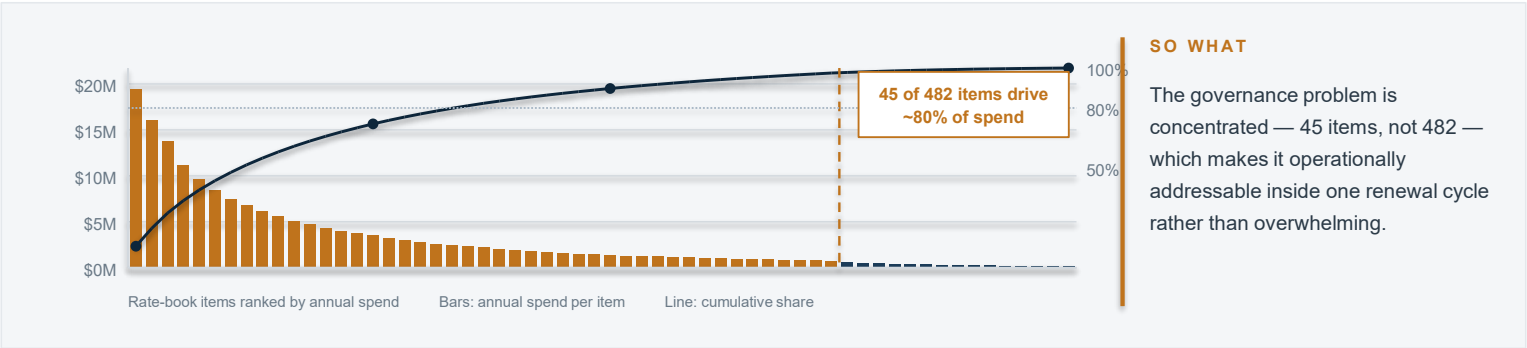


EXHIBIT 2 Above-market variance by contractor

Unit-billing variance vs the weighted-average rate · \$M



WHAT THE WORK DELIVERED

- A ~\$5–6M annual opportunity quantified against the assessment benchmark and shown to be addressable through a single structural lever.
- An RFP-ready toolkit: a five-pillar contract framework, an upgraded work-description standard and a standardised pricing template.

- Rate-book enforcement identified as that lever — avoiding a costly contractor reshuffle that would not have fixed the cause.
- A sequenced roadmap tied to the renewal critical path, each reform mapped to a specific governance failure.

HEADLINE

~\$5–6M

annual opportunity identified
